Lofthus frukt og saft

Period Highlight: #

Plan Duration | Actual Start | % Complete | Actual (beyond plan) | % Complete (beyond plan
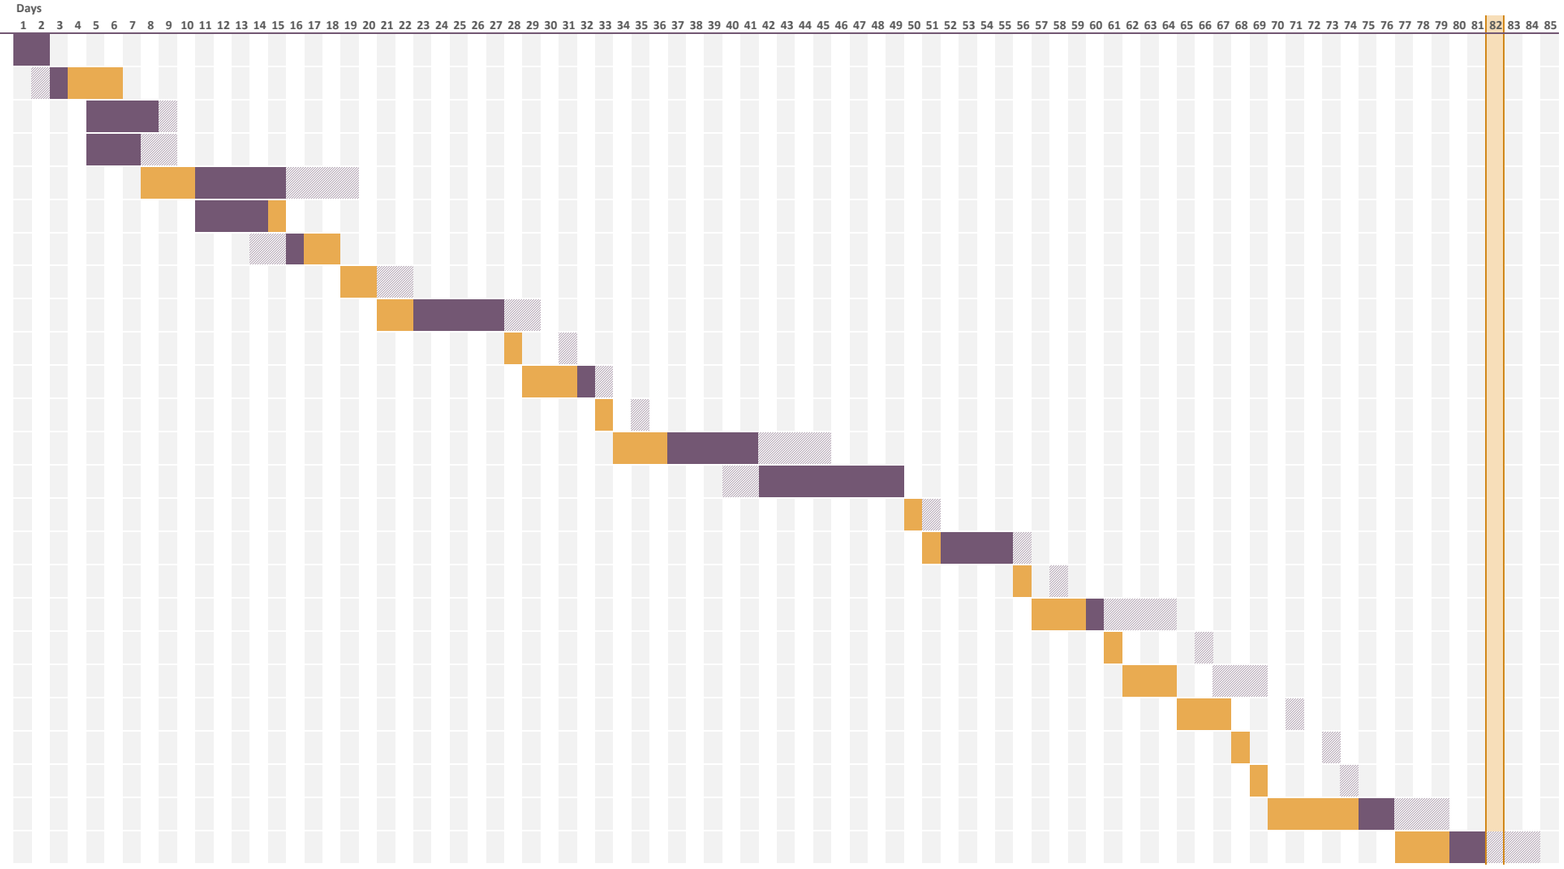
ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	RESPONSIBLE	PERCENT COMPLETE
Meeting with customer/Proposal	1	2	1	2	Interaction designer/Project manager	100 %
Contract/requirement	2	2	3	4	Project manager	100 %
Research	5	5	5	4	Interaction designer	100 %
Photograph	5	5	5	3	Photographer	100 %
Build sketch	11	9	8	8	Website designer	100 %
Edit photos	11	4	11	5	Photographer	100 %
Find material	14	3	16	3	Website designer	100 %
Improve sketch	21	2	19	2	Website designer	100 %
Style tiles	23	7	21	7	Website/Interaction designer	100 %
Present style tiles to customer	31	1	28	1	Interaction designer	100 %
Make final version of style tiles	32	2	29	4	Website/Interaction designer	100 %
Confirm final version with customer	35	1	33	1	Project manager	100 %
Build basic html code	37	9	34	8	Front end developer/Interaction designer	100 %
Add contents to each site	40	10	42	8	Front end developer	100 %
Process check meeting	51	1	50	1	Everyone	100 %
Add contents to each site 2	52	5	51	5	Front end developer	100 %
Process check meeting 2	58	1	56	1	Everyone	100 %
Make final version of website	60	5	57	4	Front end developer	100 %
Present website to customer	66	1	61	1	Interaction designer/Project manager	100 %
Adjustment of website accroding to customer	67	3	62	3	Front end developer/Interaction designer	100 %
Debug	71	1	65	3	Front end developer	100 %
Last present to customer	73	1	68	1	Interaction designer/Project manager	100 %
Publish webiste	74	1	69	1	Front end developer	100 %
User surveys	75	5	70	7	Project manager	100 %
Adjustment of website accroding surveys	80	5	77	5	Interaction designer/Project manager	100 %
